ID	Task Mode	Task Name	Duration	Start	Finish
1		**SWE574-Horuscope**	**87 days?**	**Mon 2/10/20**	**Tue 6/9/20**
2		**Planning**	**17 days**	**Mon 2/10/20**	**Tue 3/3/20**
3		Team Setup	1 day	Mon 2/10/20	Mon 2/10/20
4		Team Manifesto	1 day	Tue 2/11/20	Tue 2/11/20
5		Repository Setup	1 day	Wed 2/12/20	Wed 2/12/20
6		Wiki Setup	1 day	Thu 2/13/20	Thu 2/13/20
7		Communication Setup	1 day	Tue 2/11/20	Tue 2/11/20
8		Technology Stack	1 day	Thu 2/13/20	Thu 2/13/20
9		**Research**	**2 days**	**Fri 2/14/20**	**Mon 2/17/20**
10		W3C Activity Stream	2 days	Fri 2/14/20	Mon 2/17/20
11		W3C Web Annotation	2 days	Fri 2/14/20	Mon 2/17/20
12		Wikidata	2 days	Fri 2/14/20	Mon 2/17/20
13		Milestone 1 - Research Complete	0 days	Mon 2/17/20	Mon 2/17/20
14		Requirements Elicitaiton	10 days	Tue 2/18/20	Mon 3/2/20
15		Requirements Review	1 day	Tue 3/3/20	Tue 3/3/20
16		Milestone 2 - Requirements Complete	0 days	Tue 3/3/20	Tue 3/3/20
17		**Training**			
18		Git & Github Flow	1 day		
19		Django	2 days		
20		**Design**	**31 days**	**Wed 3/4/20**	**Wed 4/15/20**
21		Mockups	12 days	Wed 3/4/20	Thu 3/19/20
22		Class Diagrams	6 days	Fri 3/20/20	Fri 3/27/20
23		Use-case Diagrams	6 days	Mon 3/30/20	Mon 4/6/20

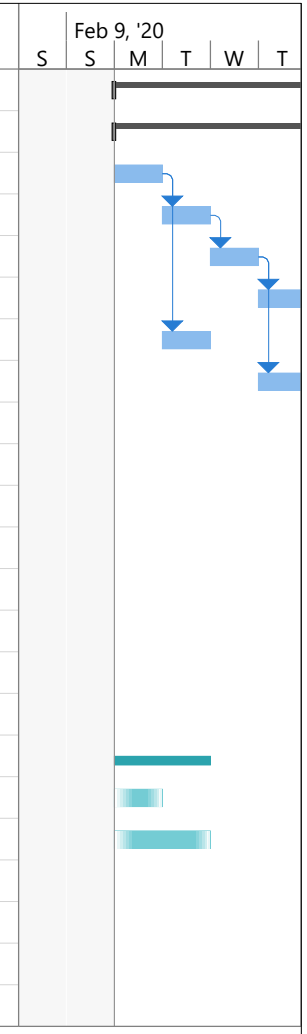

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish
24		Sequence Diagrams	6 days	Tue 4/7/20	Tue 4/14/20
25		Design Review	1 day	Wed 4/15/20	Wed 4/15/20
26		Milestone 3 - Design Complete	0 days	Wed 4/15/20	Wed 4/15/20
27		**Development**	**30 days**	**Thu 4/16/20**	**Wed 5/27/20**
28		**Web Application**	**16 days**	**Thu 4/16/20**	**Thu 5/7/20**
29		Refactor Code	1 day	Thu 4/16/20	Thu 4/16/20
30		Comment Posts	5 days	Fri 4/17/20	Thu 4/23/20
31		Flag Posts	5 days	Fri 4/24/20	Thu 4/30/20
32		Flag Moderation	5 days	Fri 5/1/20	Thu 5/7/20
33		Advanced Subscription	5 days	Fri 4/17/20	Thu 4/23/20
34		User Profile	5 days	Fri 4/17/20	Thu 4/23/20
35		Activity Stream	10 days	Fri 4/24/20	Thu 5/7/20
36		Semantic Search	10 days	Fri 4/17/20	Thu 4/30/20
37		Milestone 4 - Web Application Complete	0 days	Thu 5/7/20	Thu 5/7/20
38		**Annotation Server**	**12 days**	**Thu 4/16/20**	**Fri 5/1/20**
39		Create New Application	1 day	Thu 4/16/20	Thu 4/16/20
40		Login & Authentication	3 days	Fri 4/17/20	Tue 4/21/20
41		Save Annotation	4 days	Wed 4/22/20	Mon 4/27/20
42		List Annotations	4 days	Tue 4/28/20	Fri 5/1/20
43		Milestone 5 - Annotation Server Complete	0 days	Fri 5/1/20	Fri 5/1/20
44		**Annotation Client**	**18 days**	**Mon 5/4/20**	**Wed 5/27/20**
45		Create New Application	1 day	Mon 5/4/20	Mon 5/4/20
46		Login & Authentication	3 days	Tue 5/5/20	Thu 5/7/20



ID	Task Mode	Task Name	Duration	Start	Finish
47		Xpath Selector	5 days	Fri 5/8/20	Thu 5/14/20
48		Create Annotation	5 days	Fri 5/15/20	Thu 5/21/20
49		View Annotations	4 days	Fri 5/22/20	Wed 5/27/20
50		Milestone 6 - Annotation Client Complete	0 days	Wed 5/27/20	Wed 5/27/20
51		**Testing**	**2 days**	**Thu 5/28/20**	**Fri 5/29/20**
52		**Unit Tests**	**2 days**	**Thu 5/28/20**	**Fri 5/29/20**
53		Web Application	2 days	Thu 5/28/20	Fri 5/29/20
54		Annotation Server	2 days	Thu 5/28/20	Fri 5/29/20
55		Annotation Client	2 days	Thu 5/28/20	Fri 5/29/20
56		Milestone 7 - Ready For Deployment	0 days	Fri 5/29/20	Fri 5/29/20
57		**Deployment**	**3 days**	**Mon 6/1/20**	**Wed 6/3/20**
58		AWS Setup	1 day	Mon 6/1/20	Mon 6/1/20
59		**Annotation Client**	**2 days**	**Tue 6/2/20**	**Wed 6/3/20**
60		Deployment Guide	1 day	Tue 6/2/20	Tue 6/2/20
61		AWS Deployment	1 day	Wed 6/3/20	Wed 6/3/20
62		**Web Application**	**2 days**	**Tue 6/2/20**	**Wed 6/3/20**
63		Deployment Guide	1 day	Tue 6/2/20	Tue 6/2/20
64		AWS Deployment	1 day	Wed 6/3/20	Wed 6/3/20
65		**Annotation Server**	**2 days**	**Tue 6/2/20**	**Wed 6/3/20**
66		Deployment Guide	1 day	Tue 6/2/20	Tue 6/2/20
67		AWS Deployment	1 day	Wed 6/3/20	Wed 6/3/20
68		Milestone 8 - Production	0 days	Wed 6/3/20	Wed 6/3/20
69		**Post-Deployment**	**2 days**	**Thu 6/4/20**	**Fri 6/5/20**

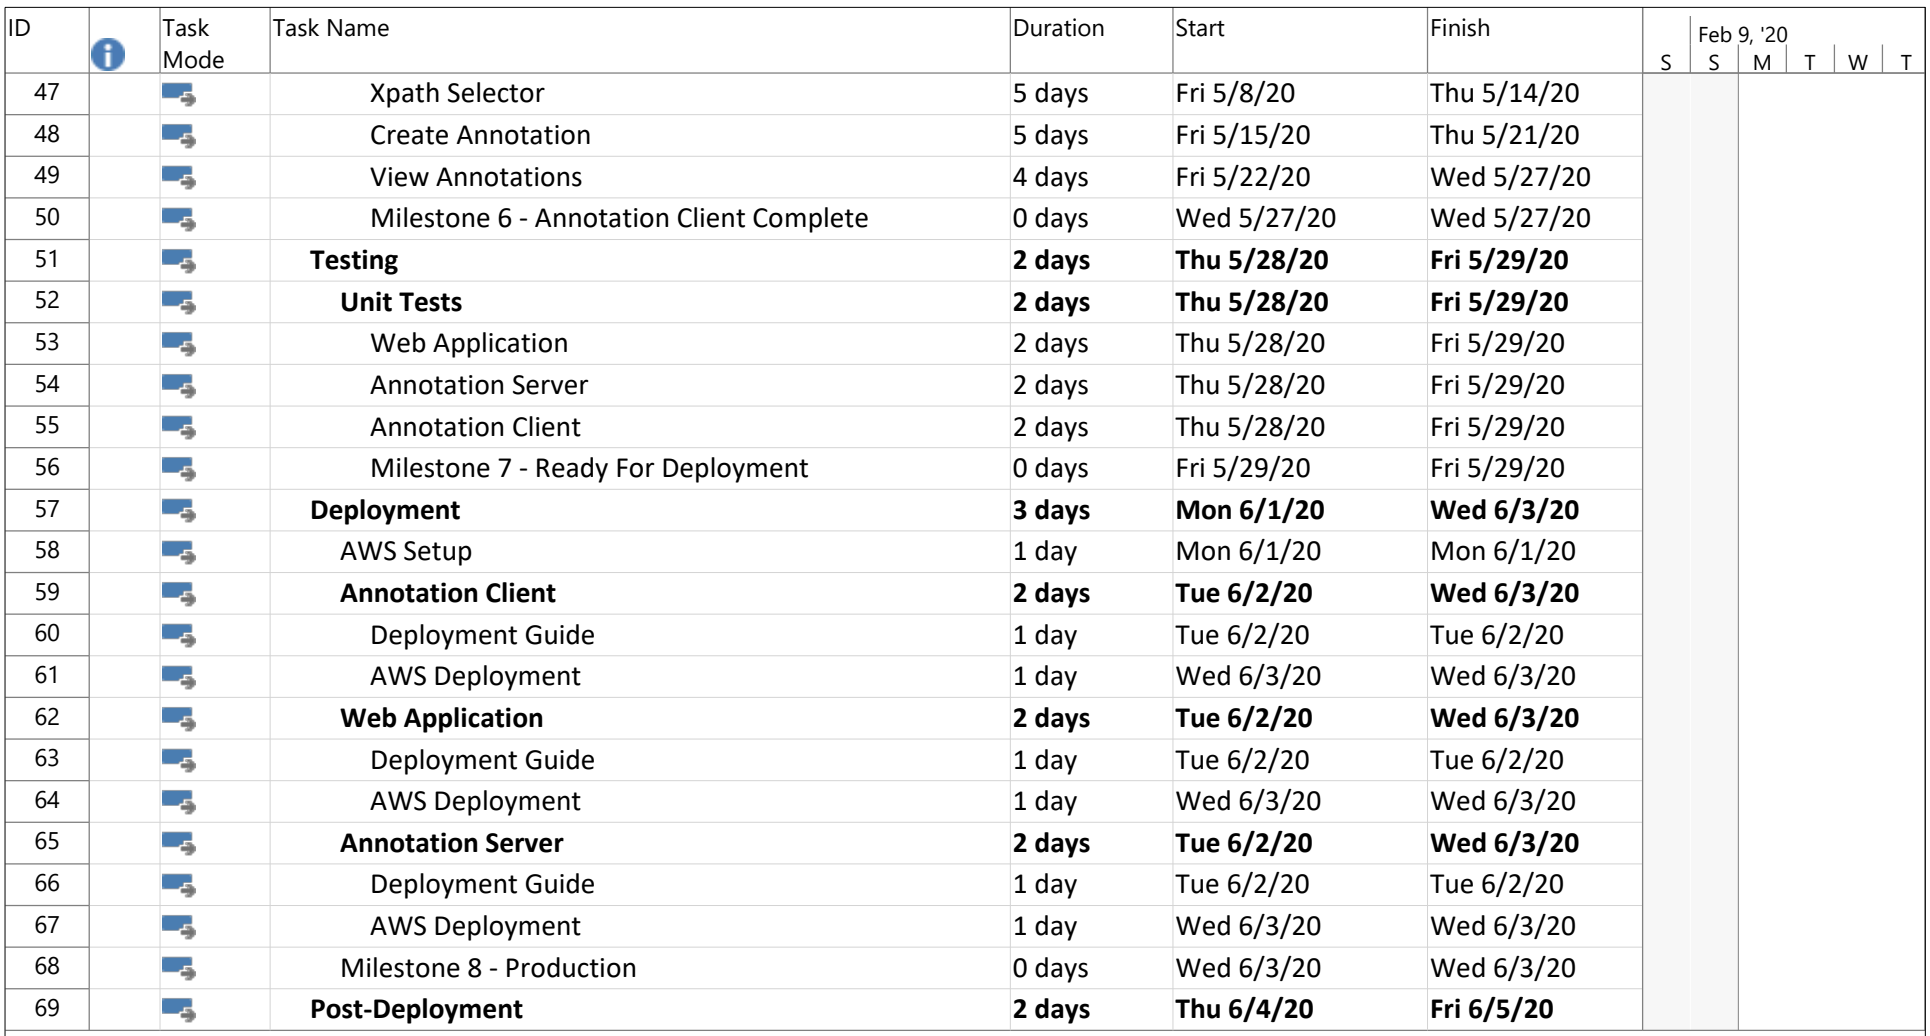

ID	Task Mode	Task Name	Duration	Start	Finish
70		Real Life Scenarios	1 day	Thu 6/4/20	Thu 6/4/20
71		Acceptance Tests	1 day	Fri 6/5/20	Fri 6/5/20
72		**Documentation**	**87 days?**	**Mon 2/10/20**	**Tue 6/9/20**
73		Research Report	1 day	Tue 2/18/20	Tue 2/18/20
74		Requirement Specification	1 day	Wed 3/4/20	Wed 3/4/20
75		Design Specification	1 day	Thu 4/16/20	Thu 4/16/20
76		Deployment Guide	1 day	Wed 6/3/20	Wed 6/3/20
77		Project Plan	1 day	Thu 4/16/20	Thu 4/16/20
78		User Manual	1 day	Mon 6/8/20	Mon 6/8/20
79		Final Report	1 day	Tue 6/9/20	Tue 6/9/20
80		Last Milestone - Project End	0 days	Tue 6/9/20	Tue 6/9/20

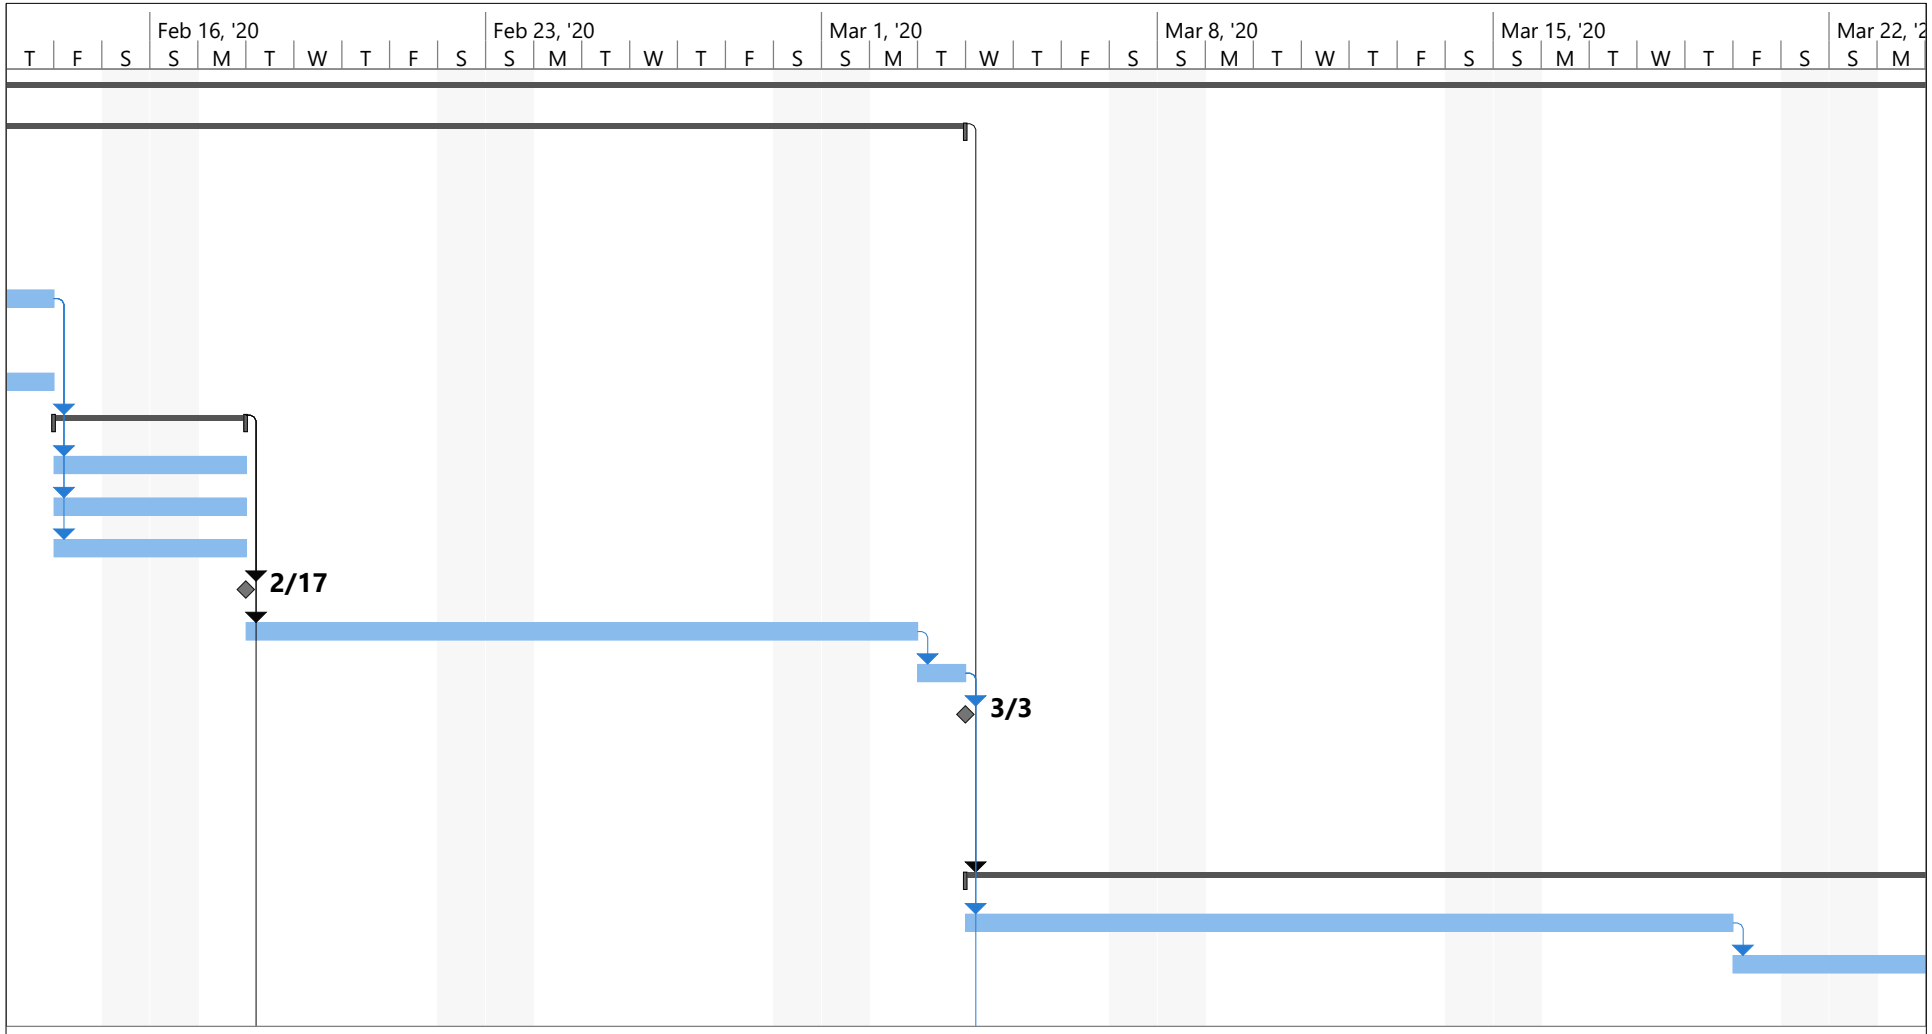

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

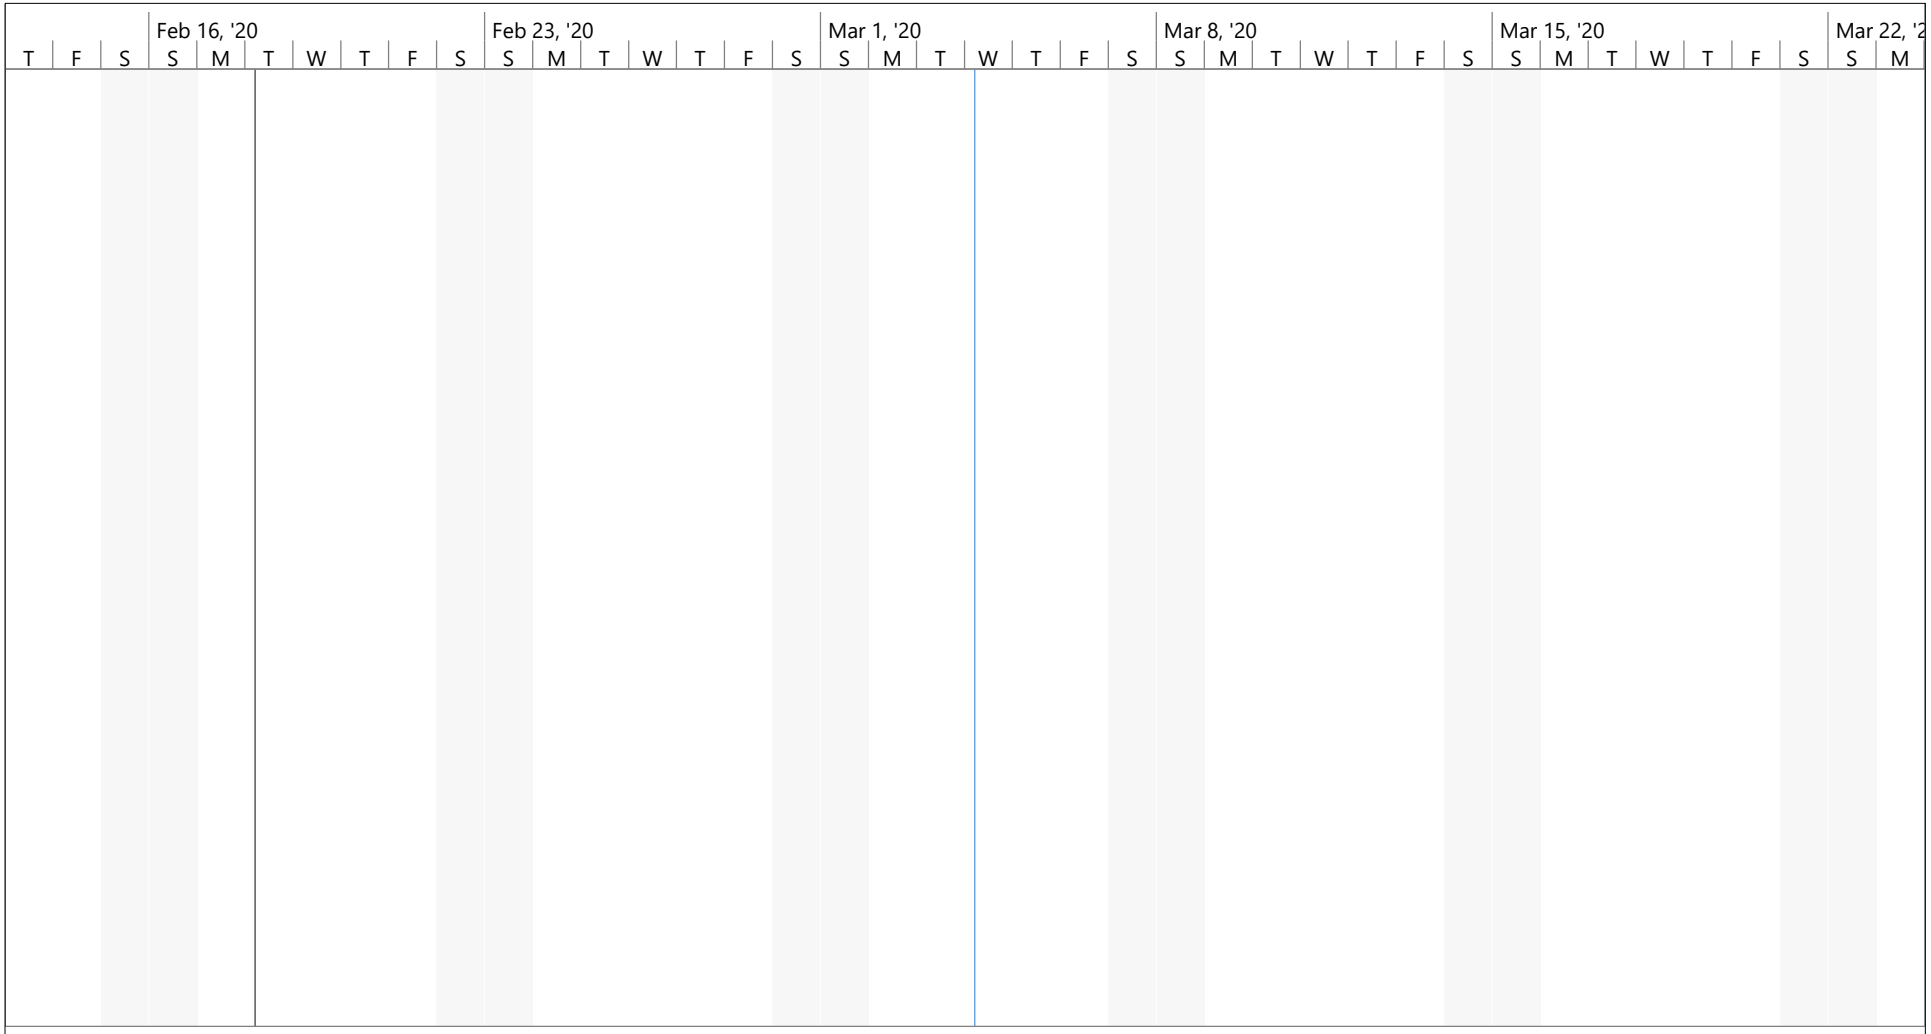

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

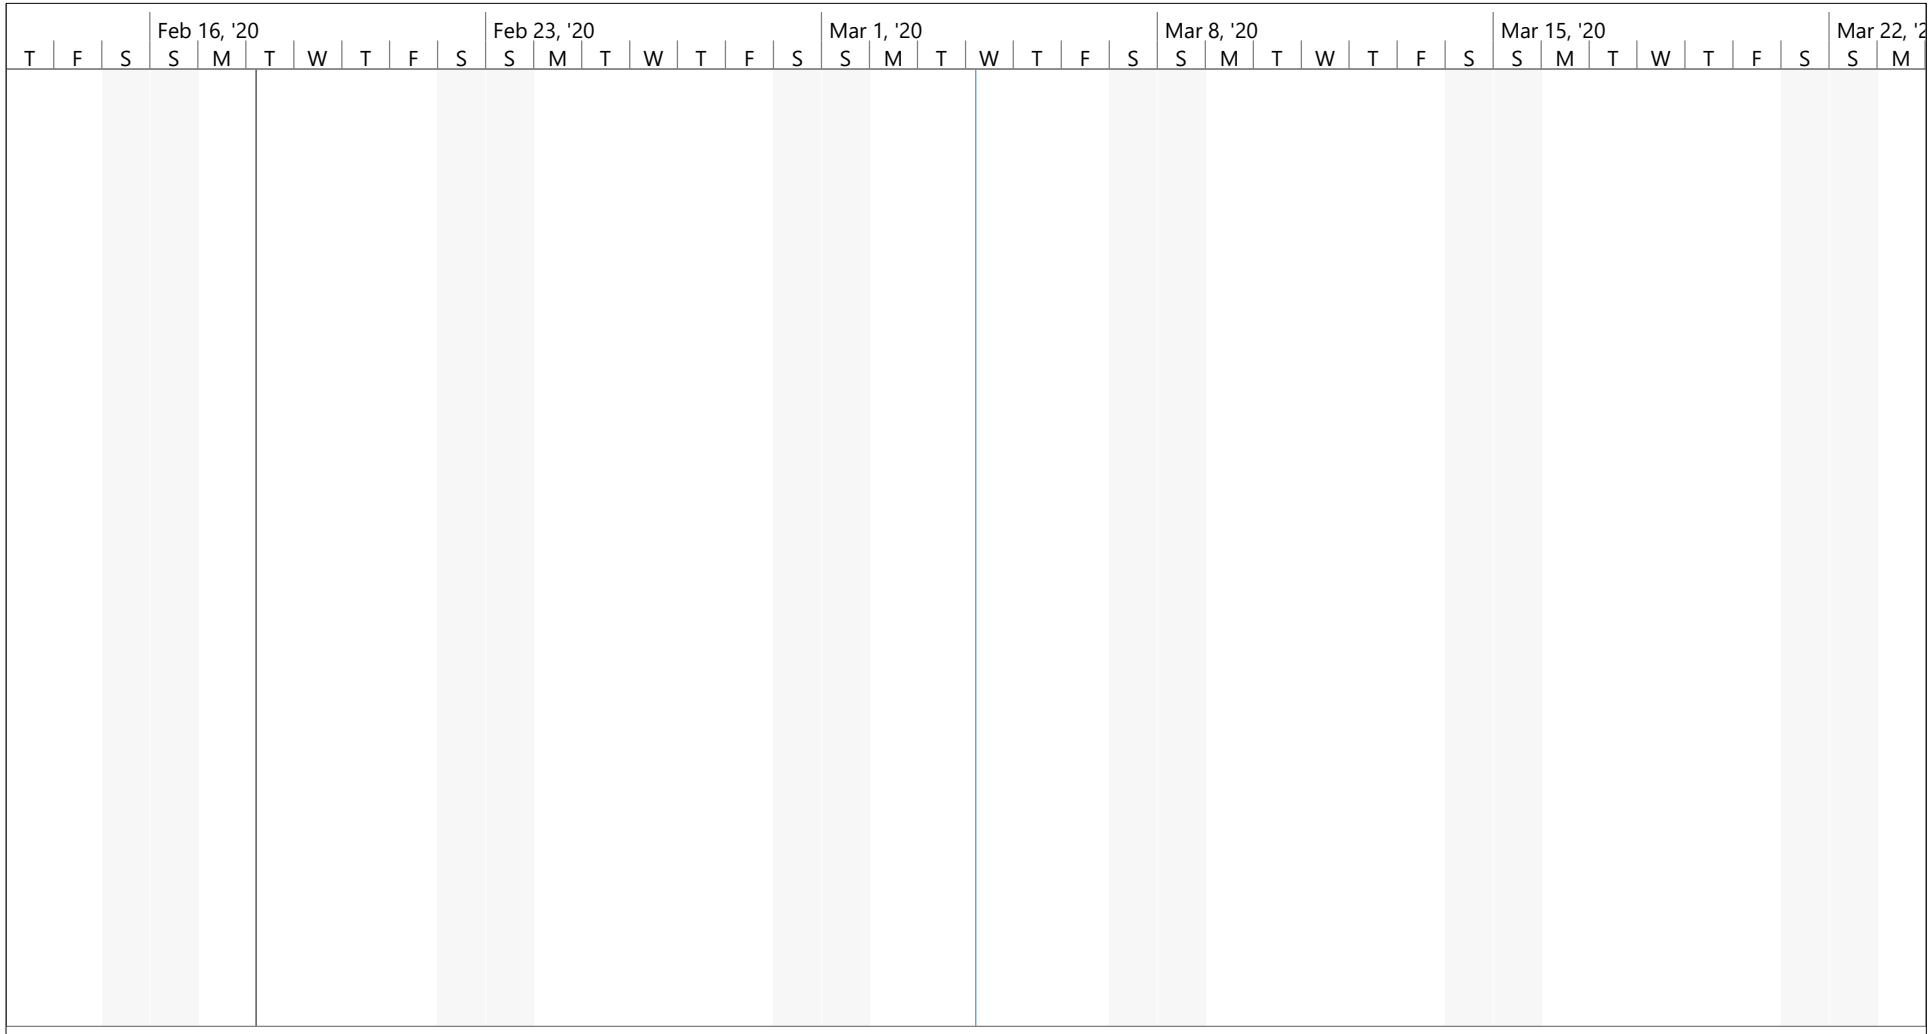

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

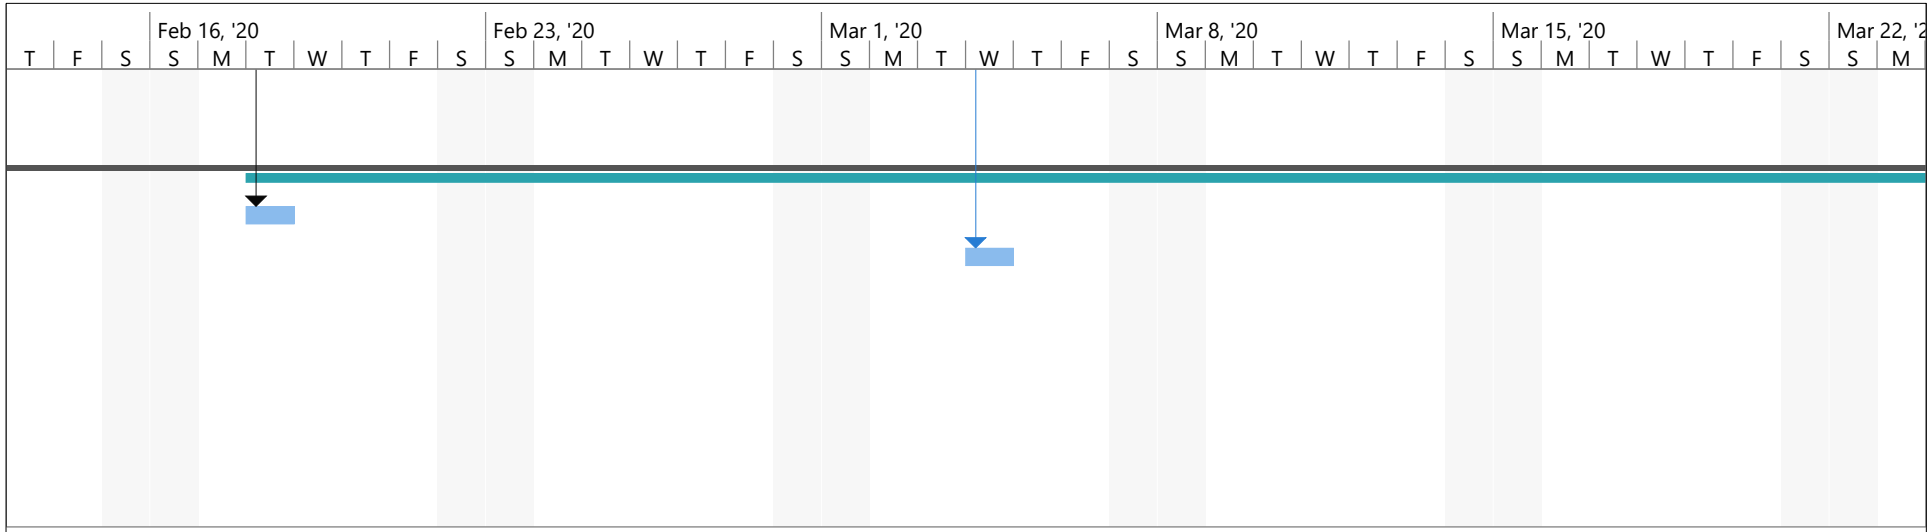

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

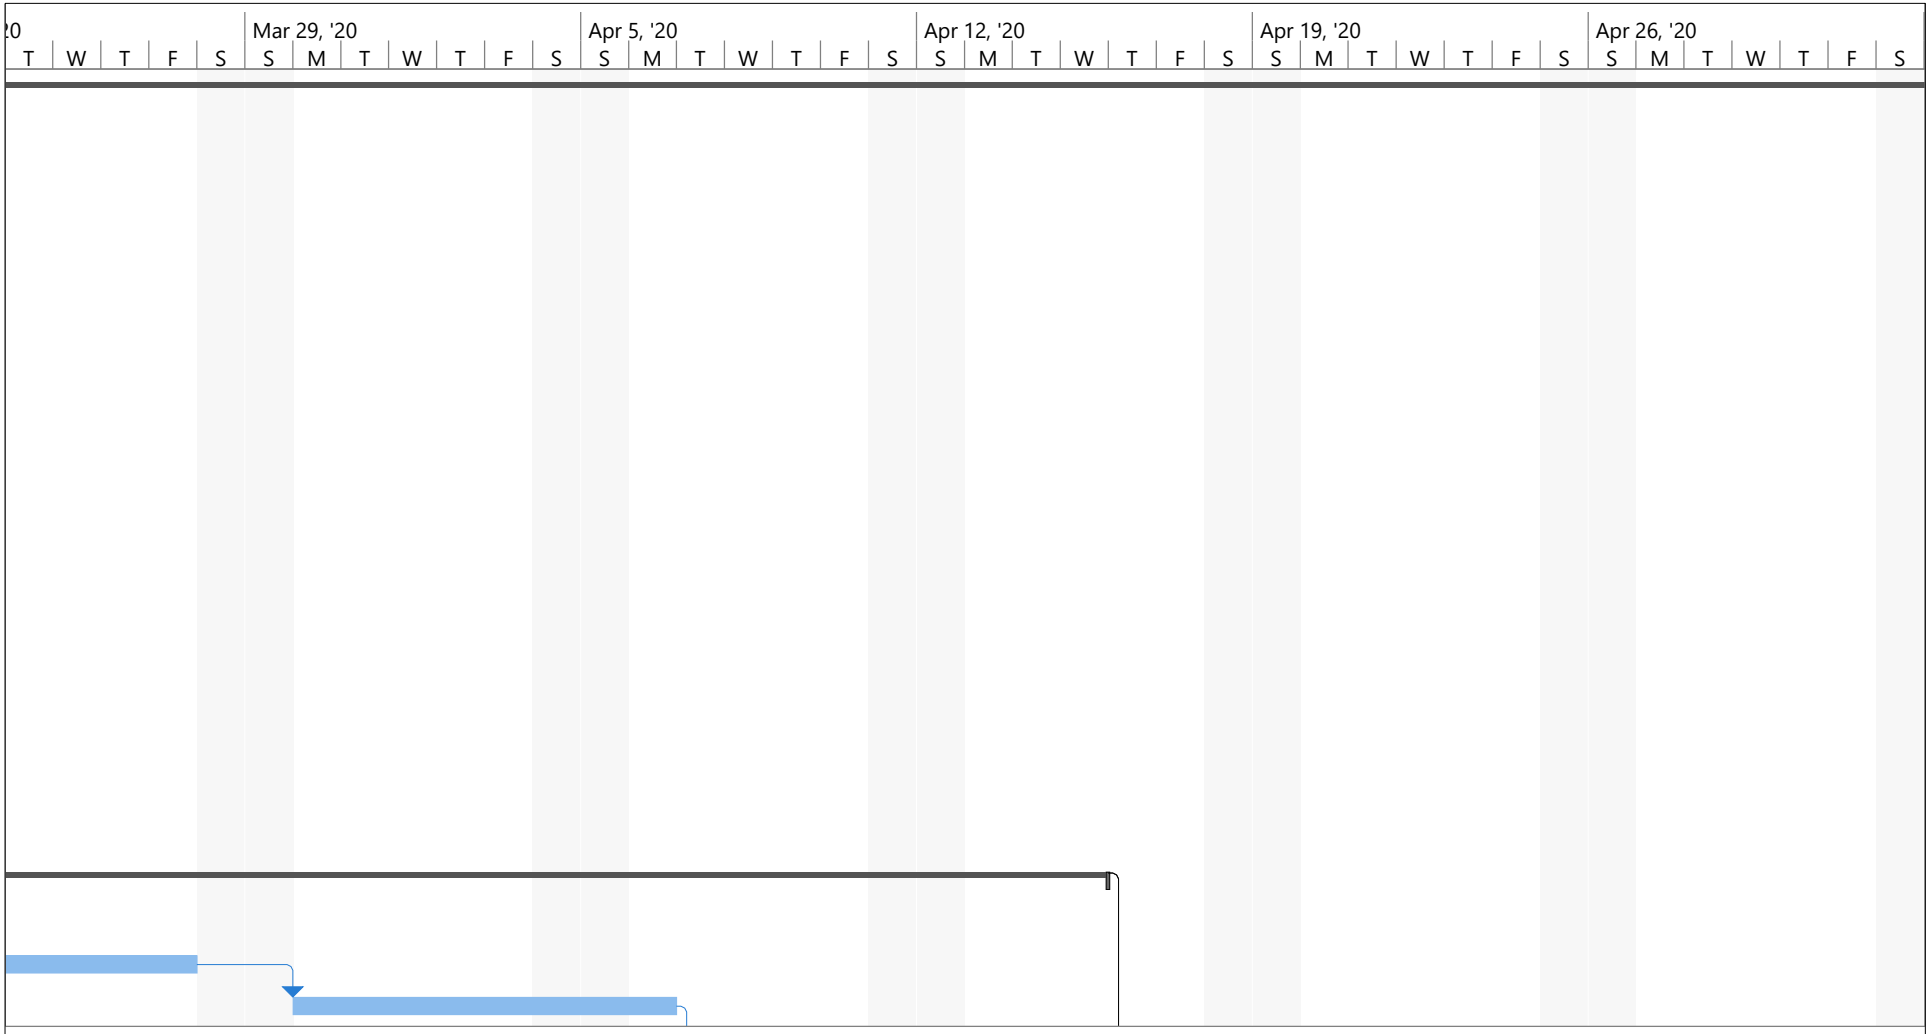

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

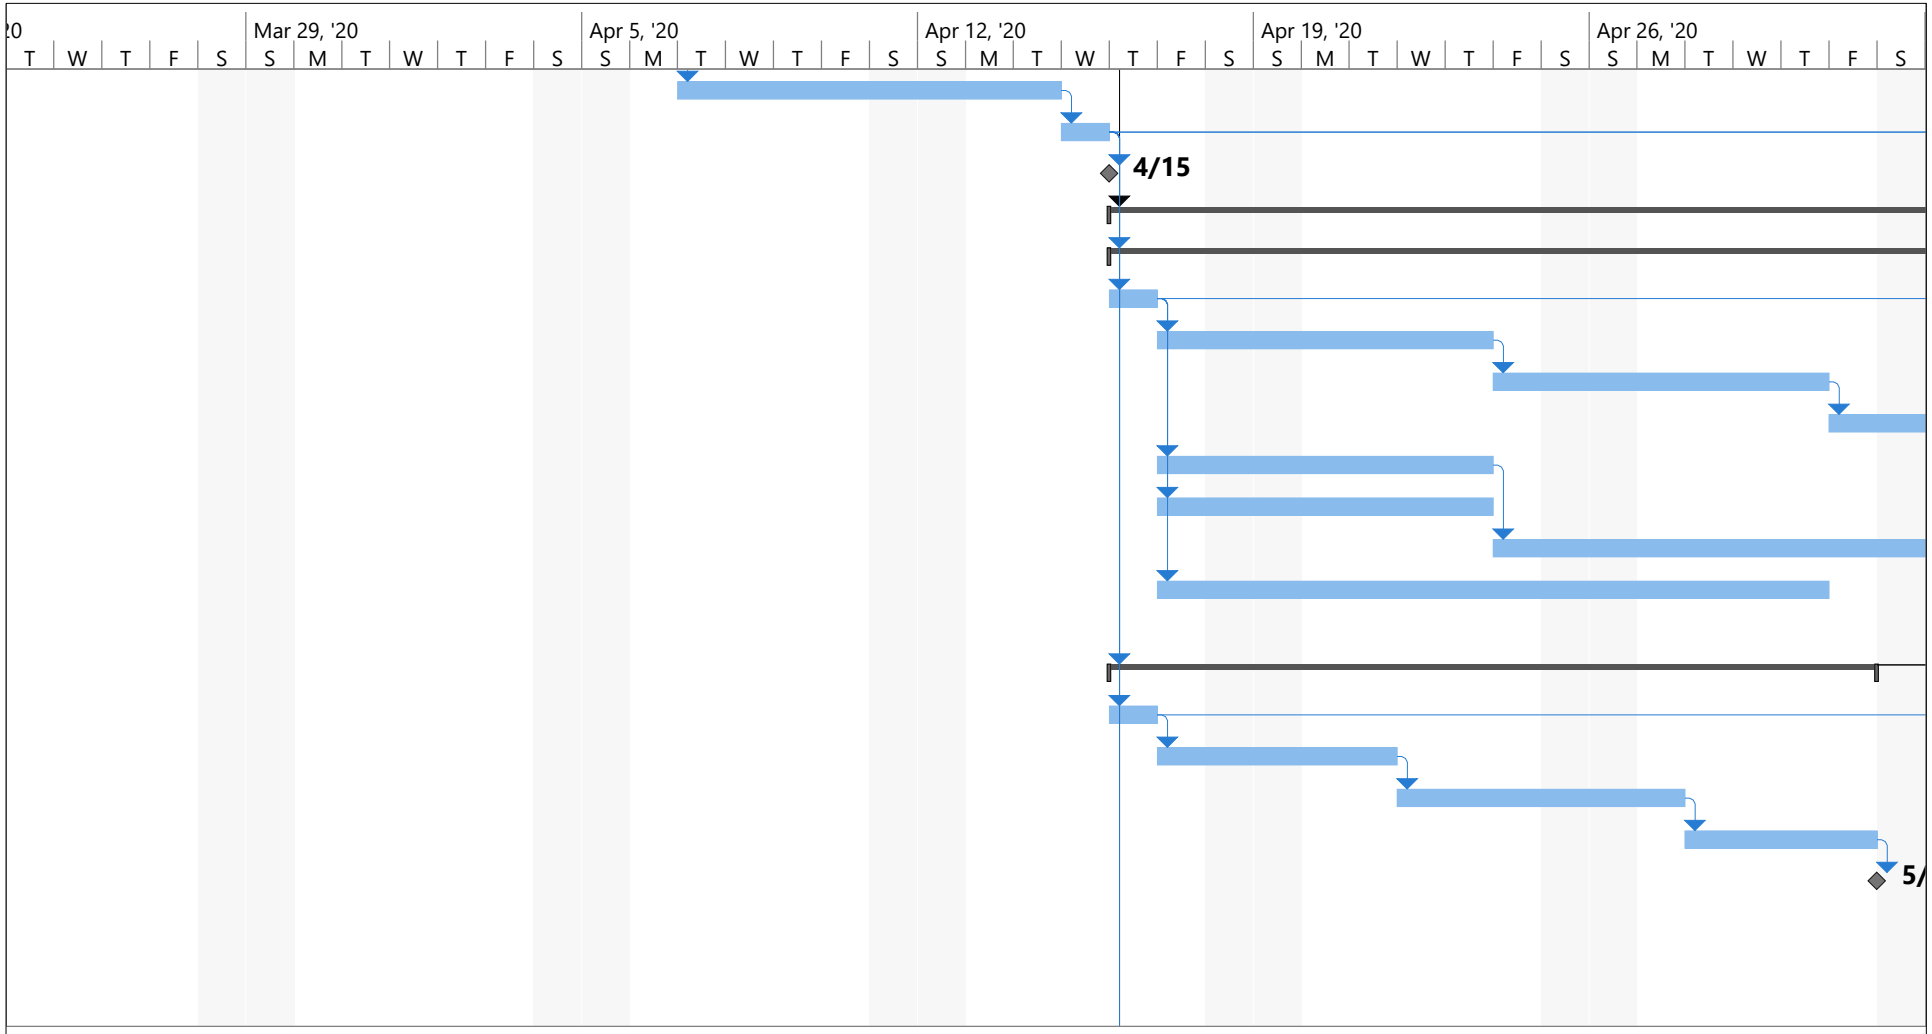

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

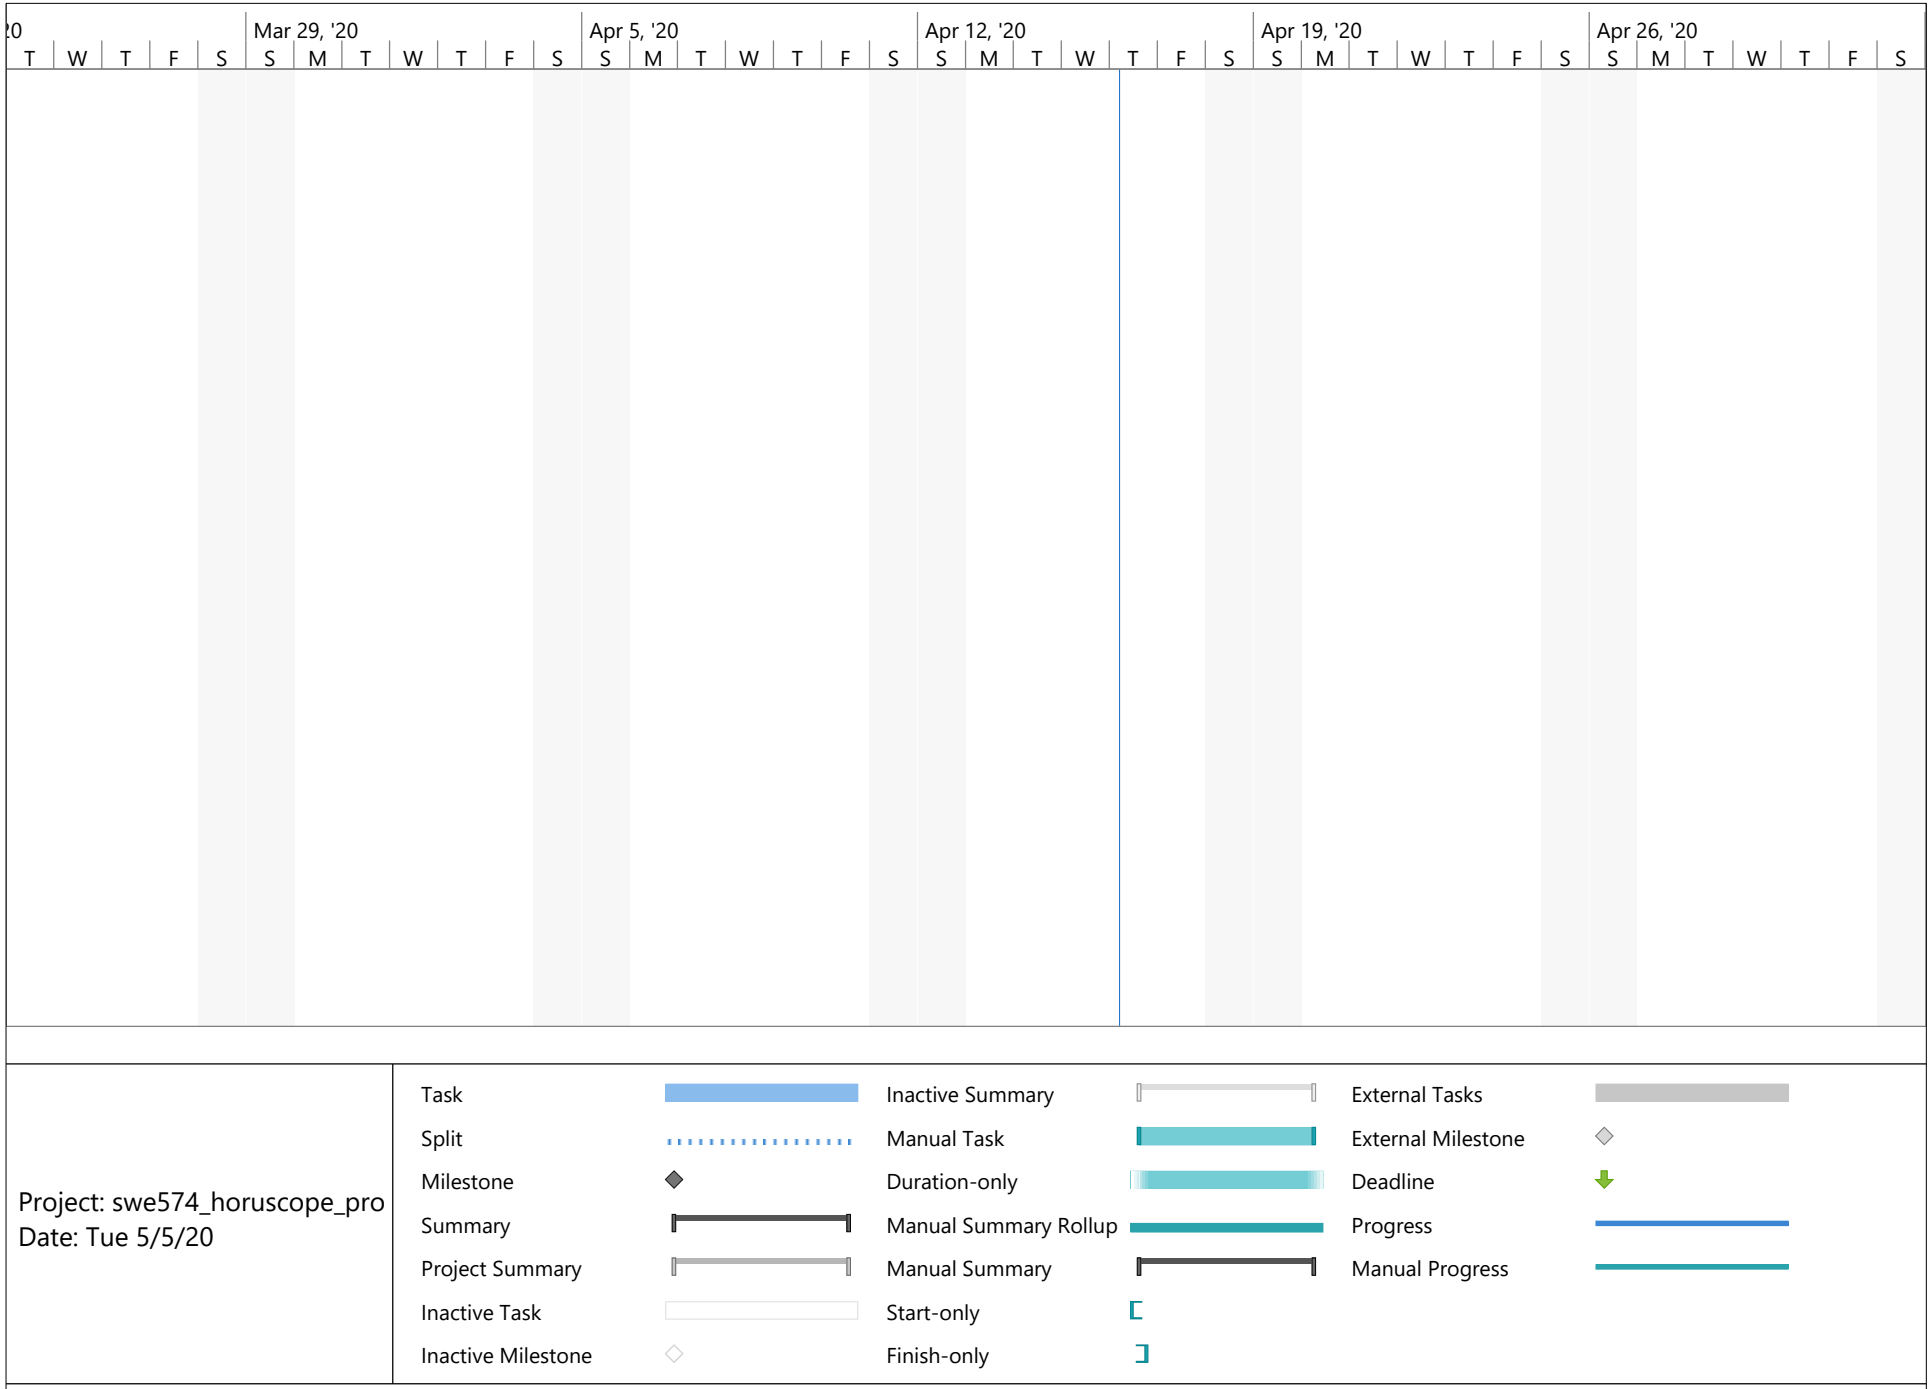

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

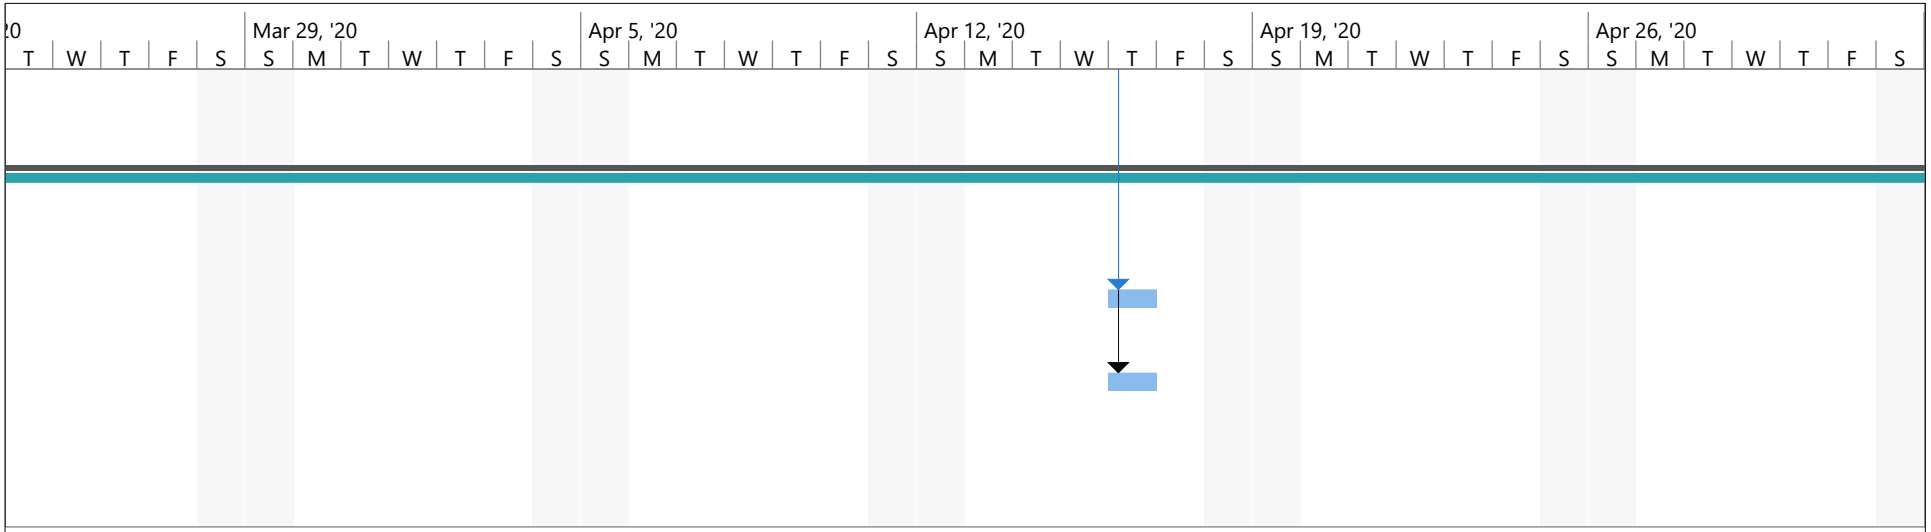

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

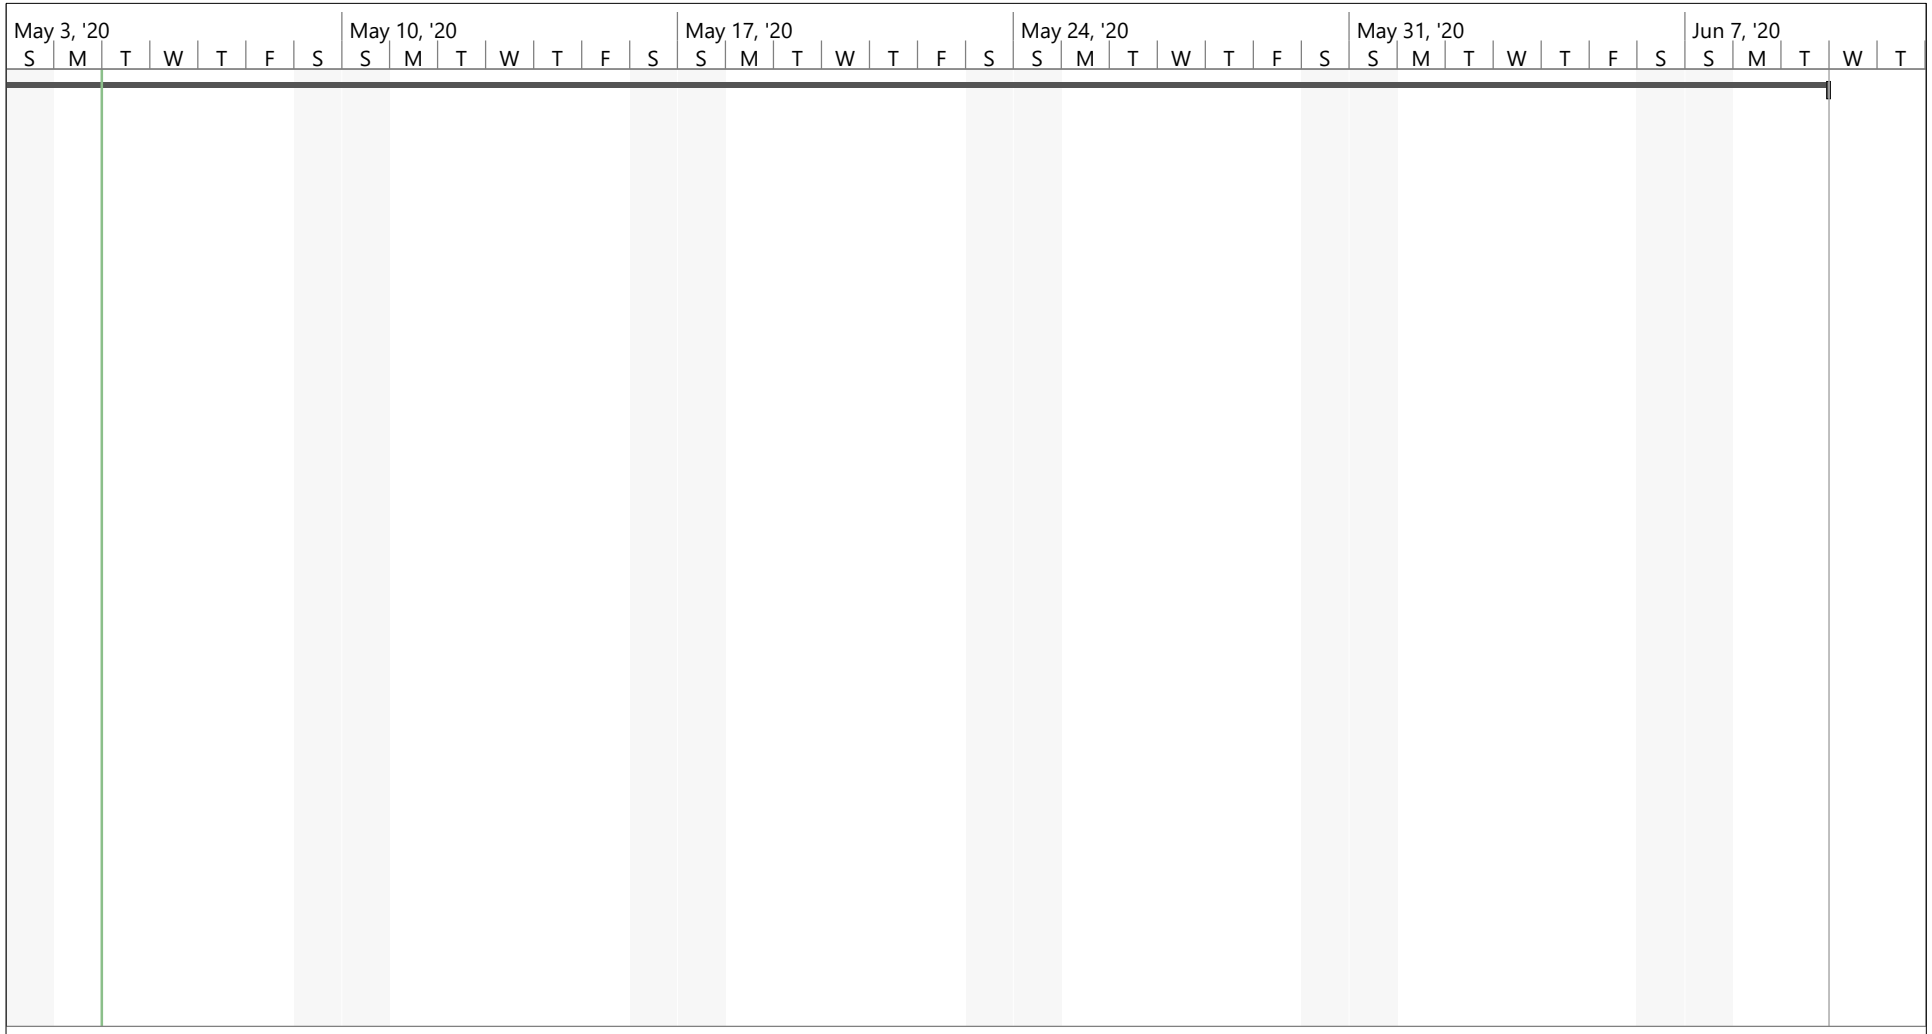

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

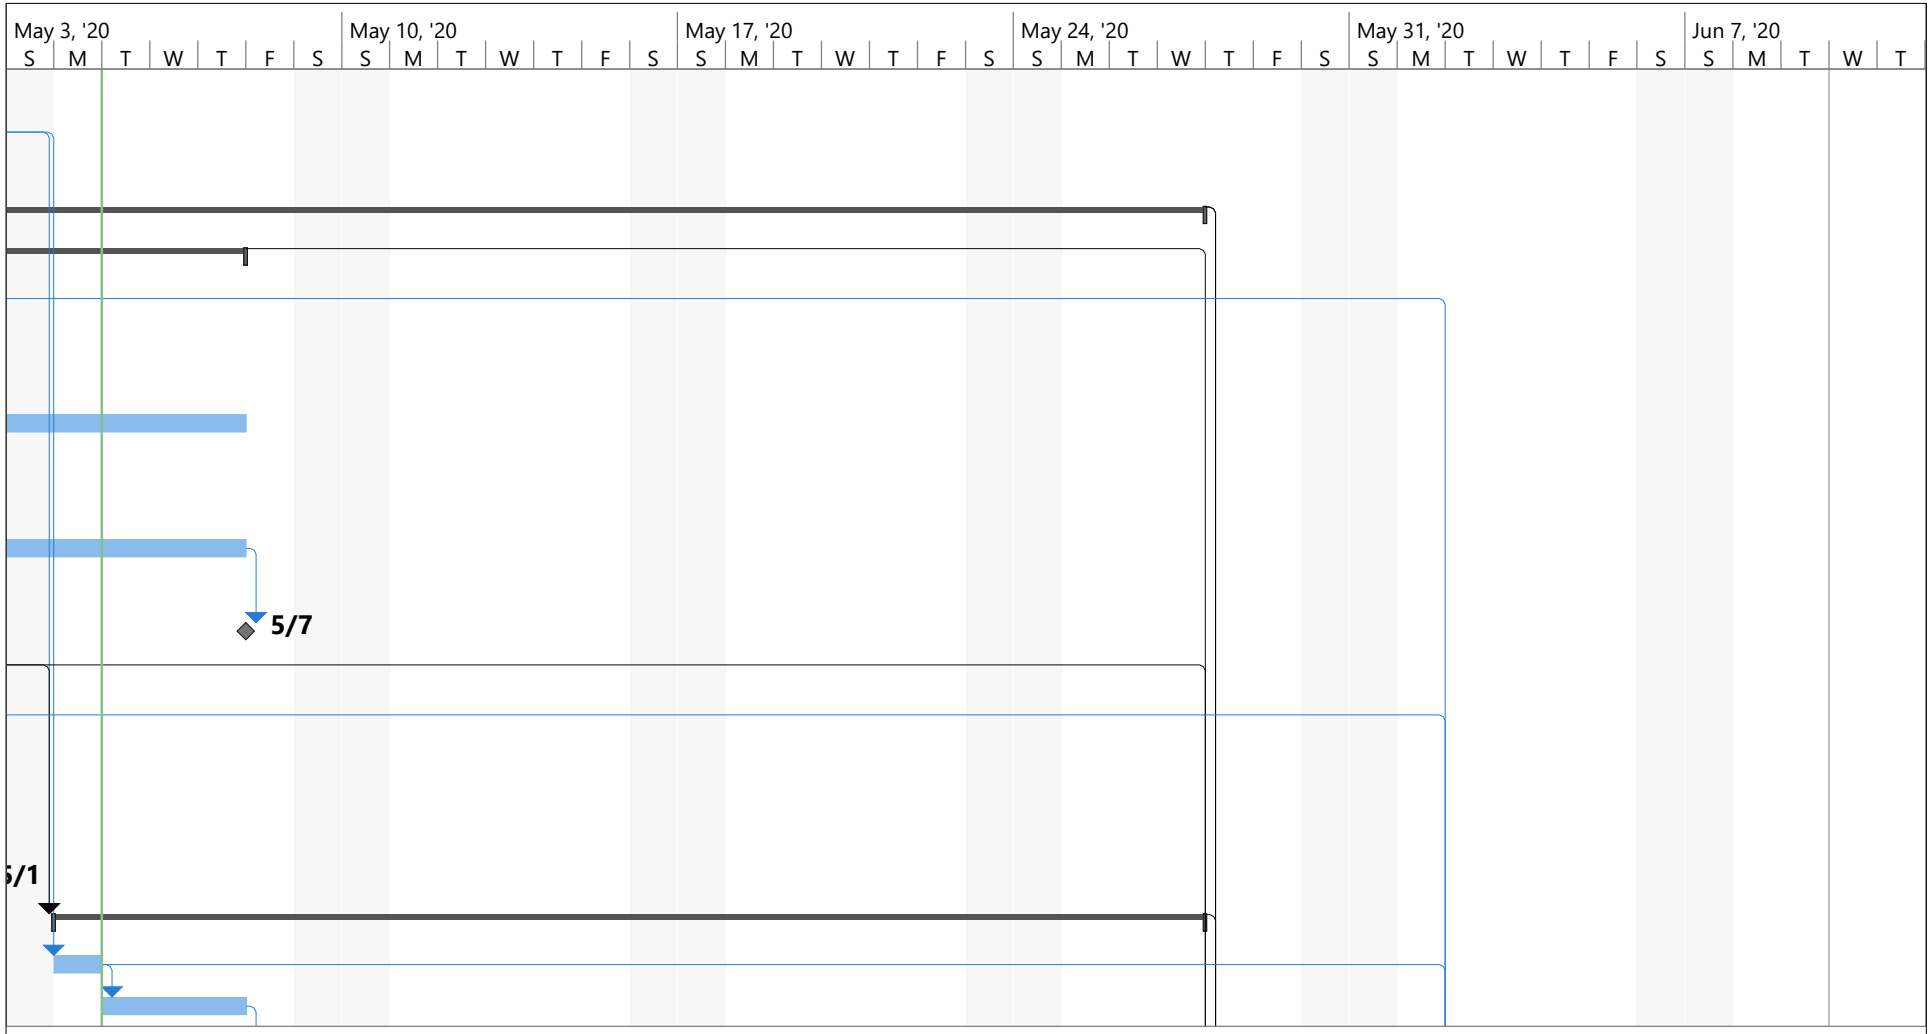

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

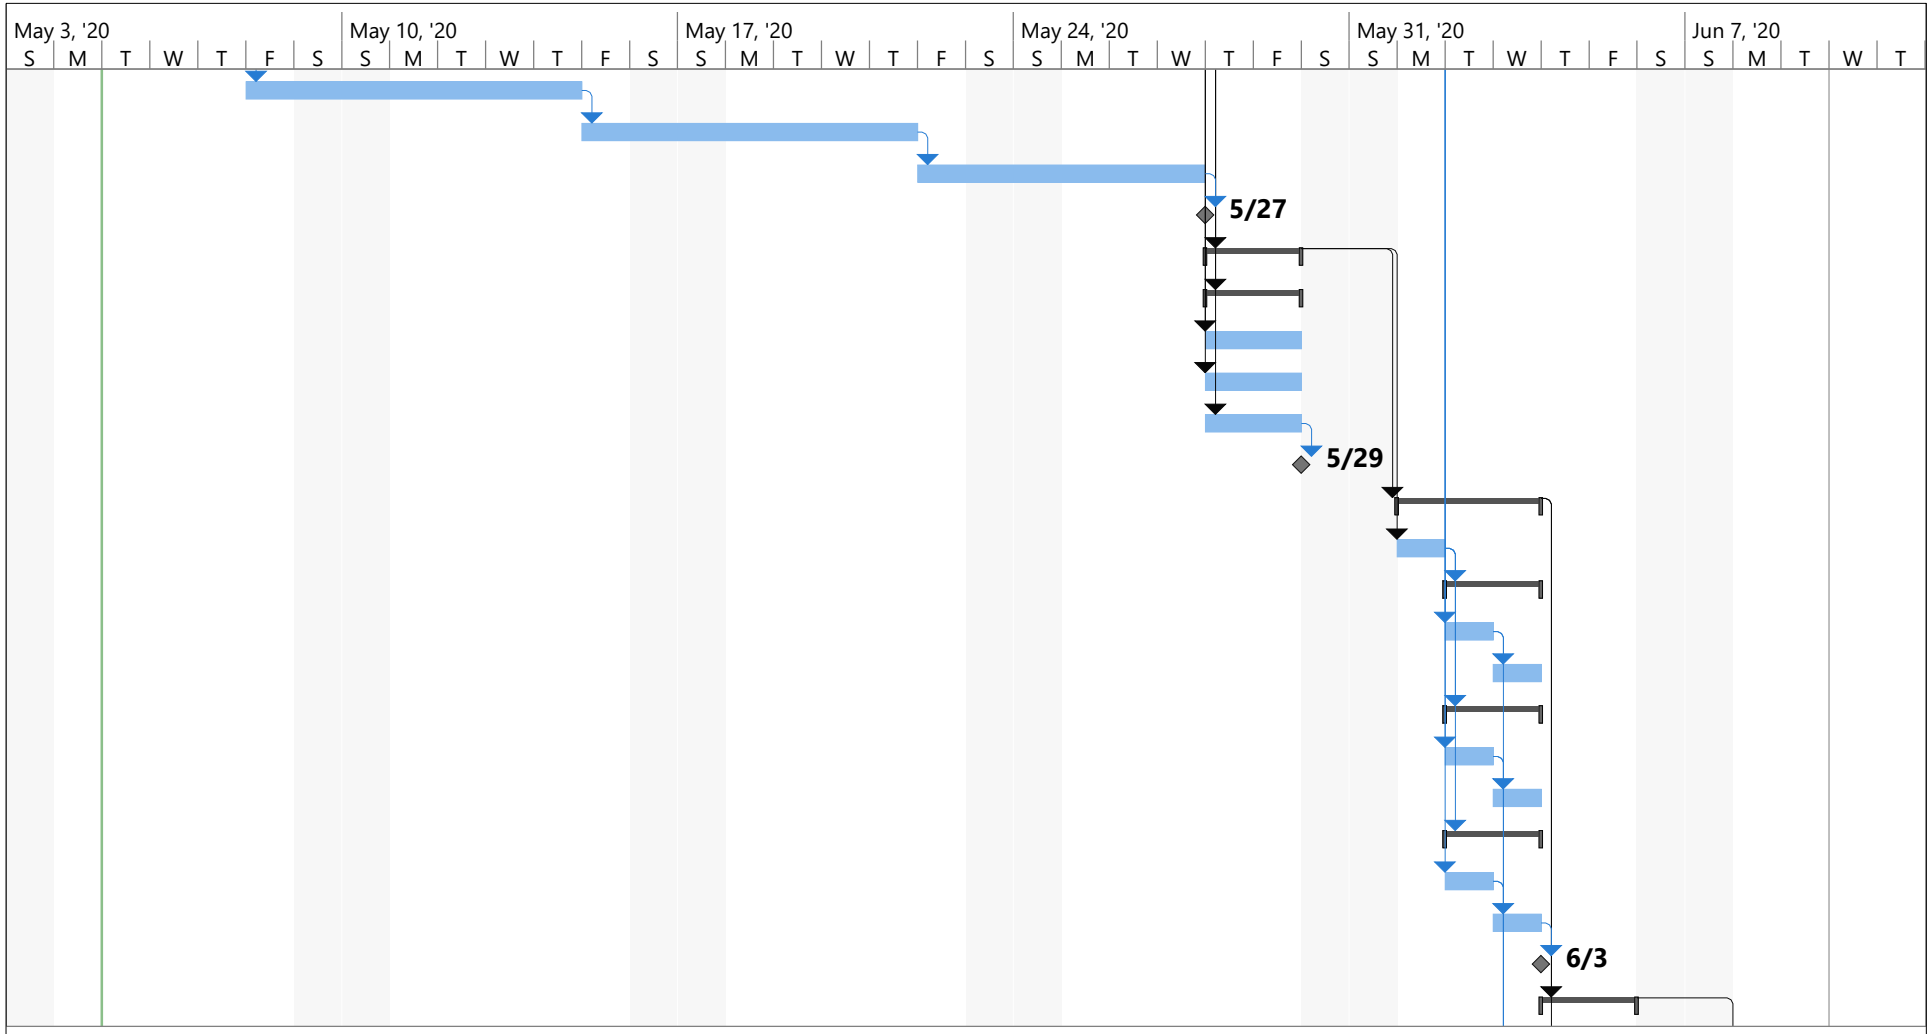

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

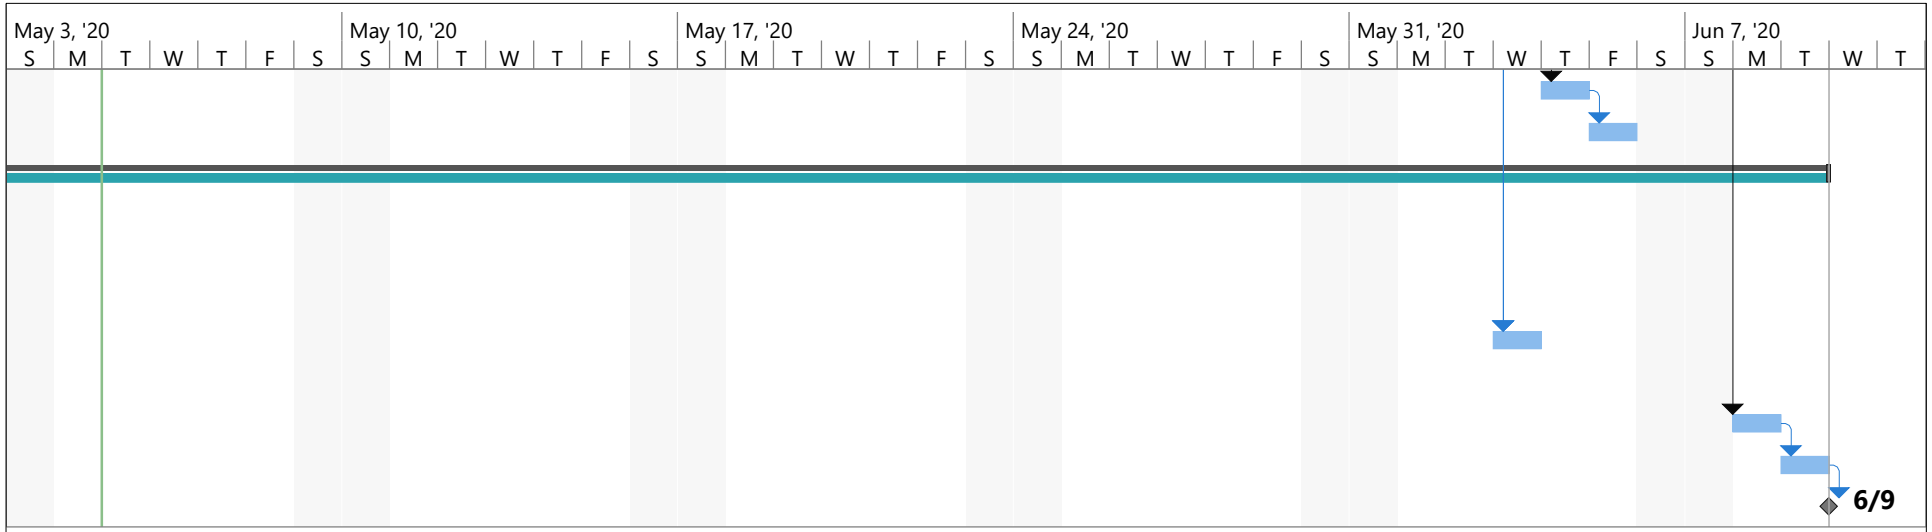

Project: swe574_horuscope_pro
Date: Tue 5/5/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	
